Hanover St Garage Restoration

Tue 2/13/24
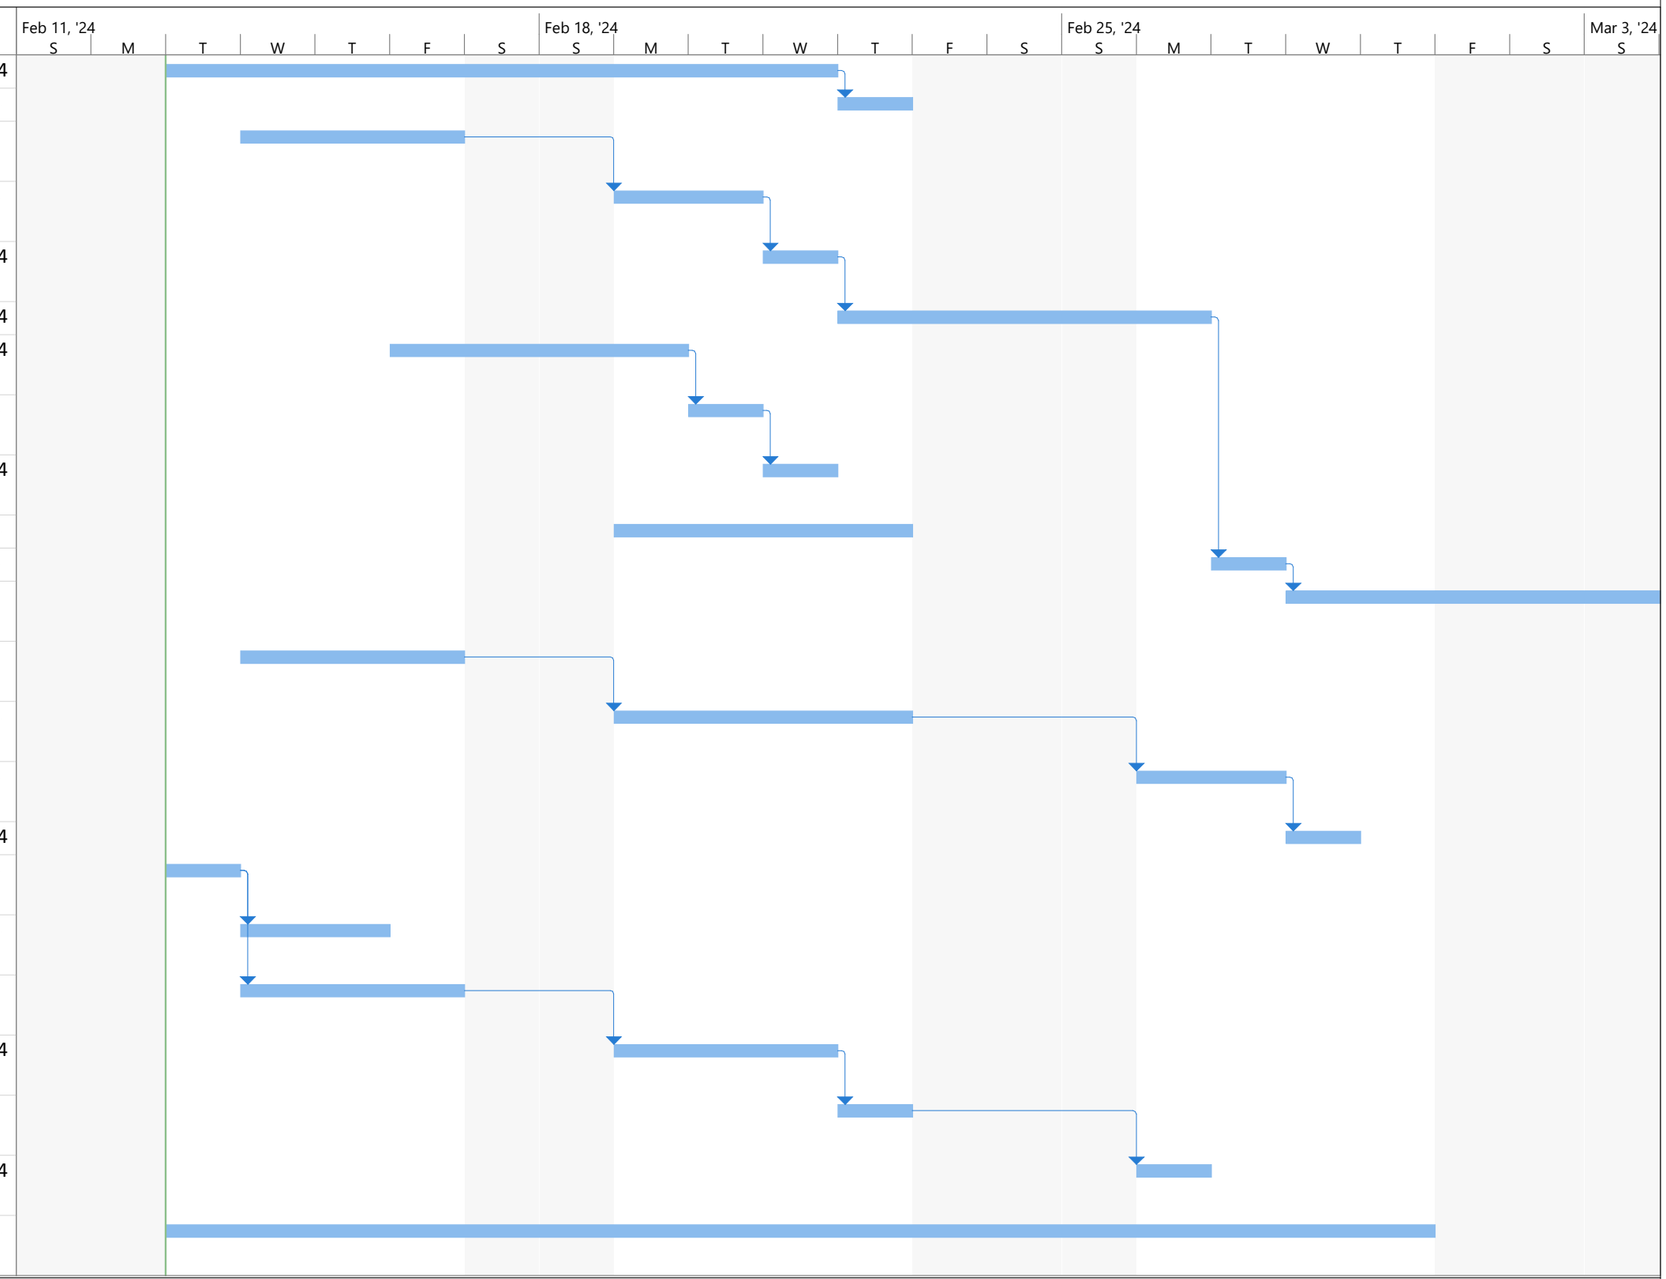
ID	Task Name	Duration	Start	Finish
1	Concrete Curing Period - Level 2	7 days	Tue 2/13/24	Wed 2/21/24
2	Remove Shoring - Level 2	1 day	Thu 2/22/24	Thu 2/22/24
3	Entrance Repairs - Level 3 - Demo (W.I. 3.1, 3.3, 3.6)	3 days	Wed 2/14/24	Fri 2/16/24
4	Entrance Repairs - Level 3 - Rebar (W.I. 3.1, 3.3, 3.6)	2 days	Mon 2/19/24	Tue 2/20/24
5	Entrance Concrete Repairs - Level 3 - Pour/Clean (W.I. 3.1, 3.3, 3.6)	1 day	Wed 2/21/24	Wed 2/21/24
6	Concrete Curing Period - Level 3	2 days	Thu 2/22/24	Mon 2/26/24
7	Underside Repairs - Level 3 - Demo (W.I. 4.1, 4.2)	2 days	Fri 2/16/24	Mon 2/19/24
8	Underside Repairs - Level 3 - Rebar (W.I. 4.1, 4.2)	1 day	Tue 2/20/24	Tue 2/20/24
9	Underside Repairs - Level 3 - Pour (W.I. 4.1, 4.2)	1 day	Wed 2/21/24	Wed 2/21/24
10	Sealant Work - Level 2 (W.I. 11.1, 11.2, 11.	4 days	Mon 2/19/24	Thu 2/22/24
11	Remove Shoring - Level 3	1 day	Tue 2/27/24	Tue 2/27/24
12	Entrance Concrete Repairs - Level 2 - Demo (W.I. 3.1, 3.3, 3.6)	3 days	Wed 2/28/24	Mon 3/4/24
13	Column Repair - Level 1 - Shoring (W.I. 6.6, 6.7)	3 days	Wed 2/14/24	Fri 2/16/24
14	Column Repair - Level 1 - Demo (W.I. 6.6, 6.7)	4 days	Mon 2/19/24	Thu 2/22/24
15	Column Repair - Level 1 - Rebar (W.I. 6.6, 6.7)	2 days	Mon 2/26/24	Tue 2/27/24
16	Column Repair - Level 1 - Pour (W.I. 6.6, 6.	1 day	Wed 2/28/24	Wed 2/28/24
17	Fleet Street Stair Tower - Level 4 Landing - Pour/Clean (W.I. 41.2)	1 day	Tue 2/13/24	Tue 2/13/24
18	Fleet Street Stair Tower - PD Landing & Stair Pan Repairs (W.I. 3.11, 41.1)	2 days	Wed 2/14/24	Thu 2/15/24
19	Concrete Curing Period - Fleet St Stair Tower - Level 4	3 days	Wed 2/14/24	Fri 2/16/24
20	Fleet St Stair Tower - Level 3 Landing - Demo (W.I. 41.2)	3 days	Mon 2/19/24	Wed 2/21/24
21	Fleet St Stair Tower - Level 3 Landing - Rebar (W.I. 41.2)	1 day	Thu 2/22/24	Thu 2/22/24
22	Fleet St Stair Tower - Level 3 Landing - Pour/Clean (W.I. 41.2)	1 day	Mon 2/26/24	Mon 2/26/24
23	Sealant Work - Level 4 (W.I. 11.1, 11.2, 11.5) - Weather Dependent	12 days	Tue 2/13/24	Thu 2/29/24
