Hanover St Garage Restoration

Tue 6/18/24
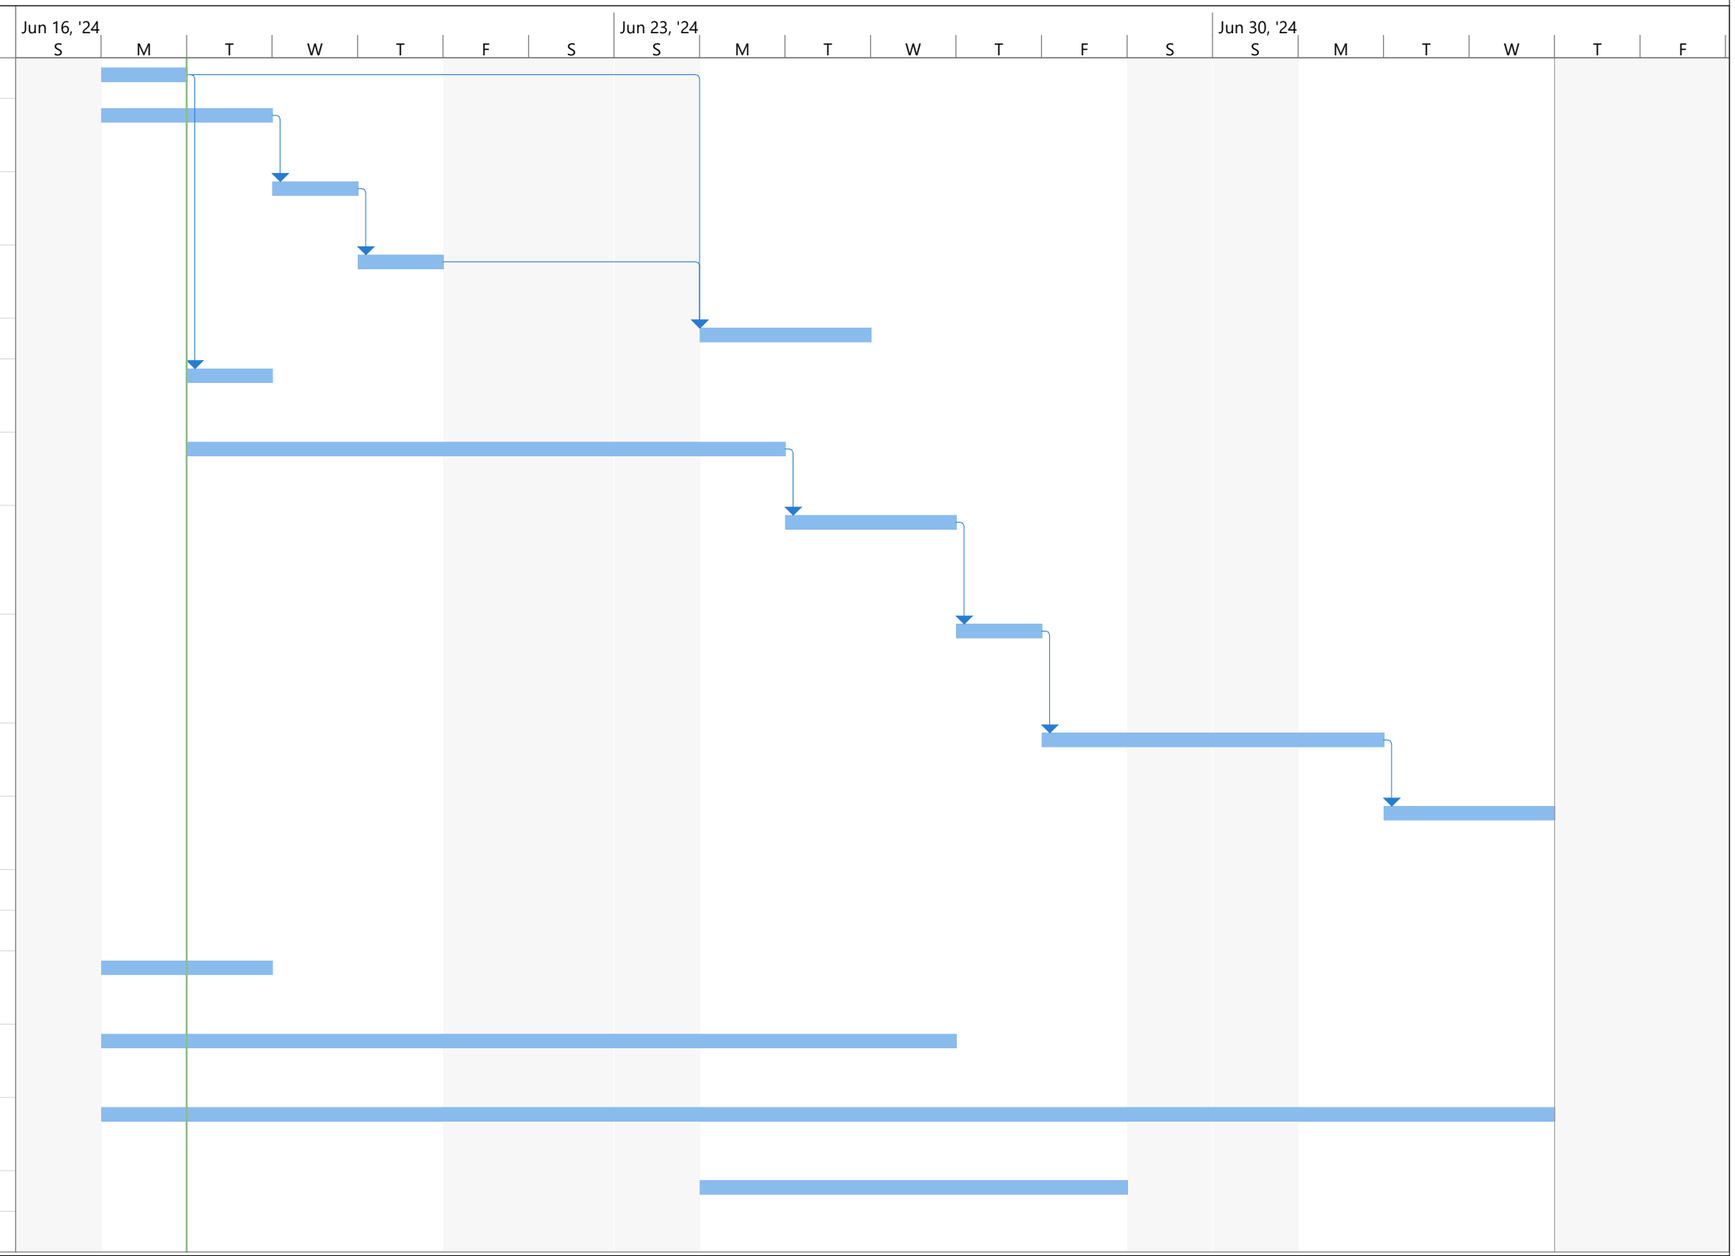
ID	Task Name	Duration	Start
1	Concrete Curing Period - Ramp 2/3	1 day	Mon 6/17/24
2	Concrete Repairs - Underside Ramp 2/3 - Demo (W.I. 4.1, 4.2)	2 days	Mon 6/17/24
3	Concrete Repairs - Underside Ramp 2/3 - Rebar and Prep (W.I. 4.1, 4.2)	1 day	Wed 6/19/24
4	Concrete Repairs - Underside Ramp 2/3 - Pour and Clean (W.I. 4.1, 4.2)	1 day	Thu 6/20/24
5	Remove Shoring and Temp Partition	2 days	Mon 6/24/24
6	Concrete Repairs - Ramp 3/4 and Level 4 - Shoring (W.I. 3.1, 3.3, 3.4 and 3.7)	1 day	Tue 6/18/24
7	Concrete Repairs - Ramp 3/4 and Level 4 - Demo (W.I. 3.1, 3.3, 3.4 and 3.7)	4 days	Tue 6/18/24
8	Concrete Repairs - Ramp 3/4 and Level 4 - Rebar and Prep (W.I. 3.1, 3.3, 3.4 and 3.7)	2 days	Tue 6/25/24
9	Concrete Repairs - Ramp 3/4 and Level 4 - Pour and Clean (W.I. 3.1, 3.3, 3.4 and 3.7)	1 day	Thu 6/27/24
10	Concrete Curing Period - Ramp 3/4 and Level 4	2 days	Fri 6/28/24
11	Concrete Repairs - Ramp 3/4 and Level 4 - Remove Shoring	2 days	Tue 7/2/24
12			
13			
14	Sealant Work - Ramp 3/4 (W.I. 11.1, 11.2, 11.5)	2 days	Mon 6/17/24
15	Sealant Work - Ramp 2/3 (W.I. 11.1, 11.2, 11.5)	7 days	Mon 6/17/24
16	Sealant Work - Garage Addition - Levels 4	12 days	Mon 6/17/24
17	Expansion Joint - Level 4	5 days	Mon 6/24/24
18
