Hanover St Garage Restoration

Thu 8/22/24
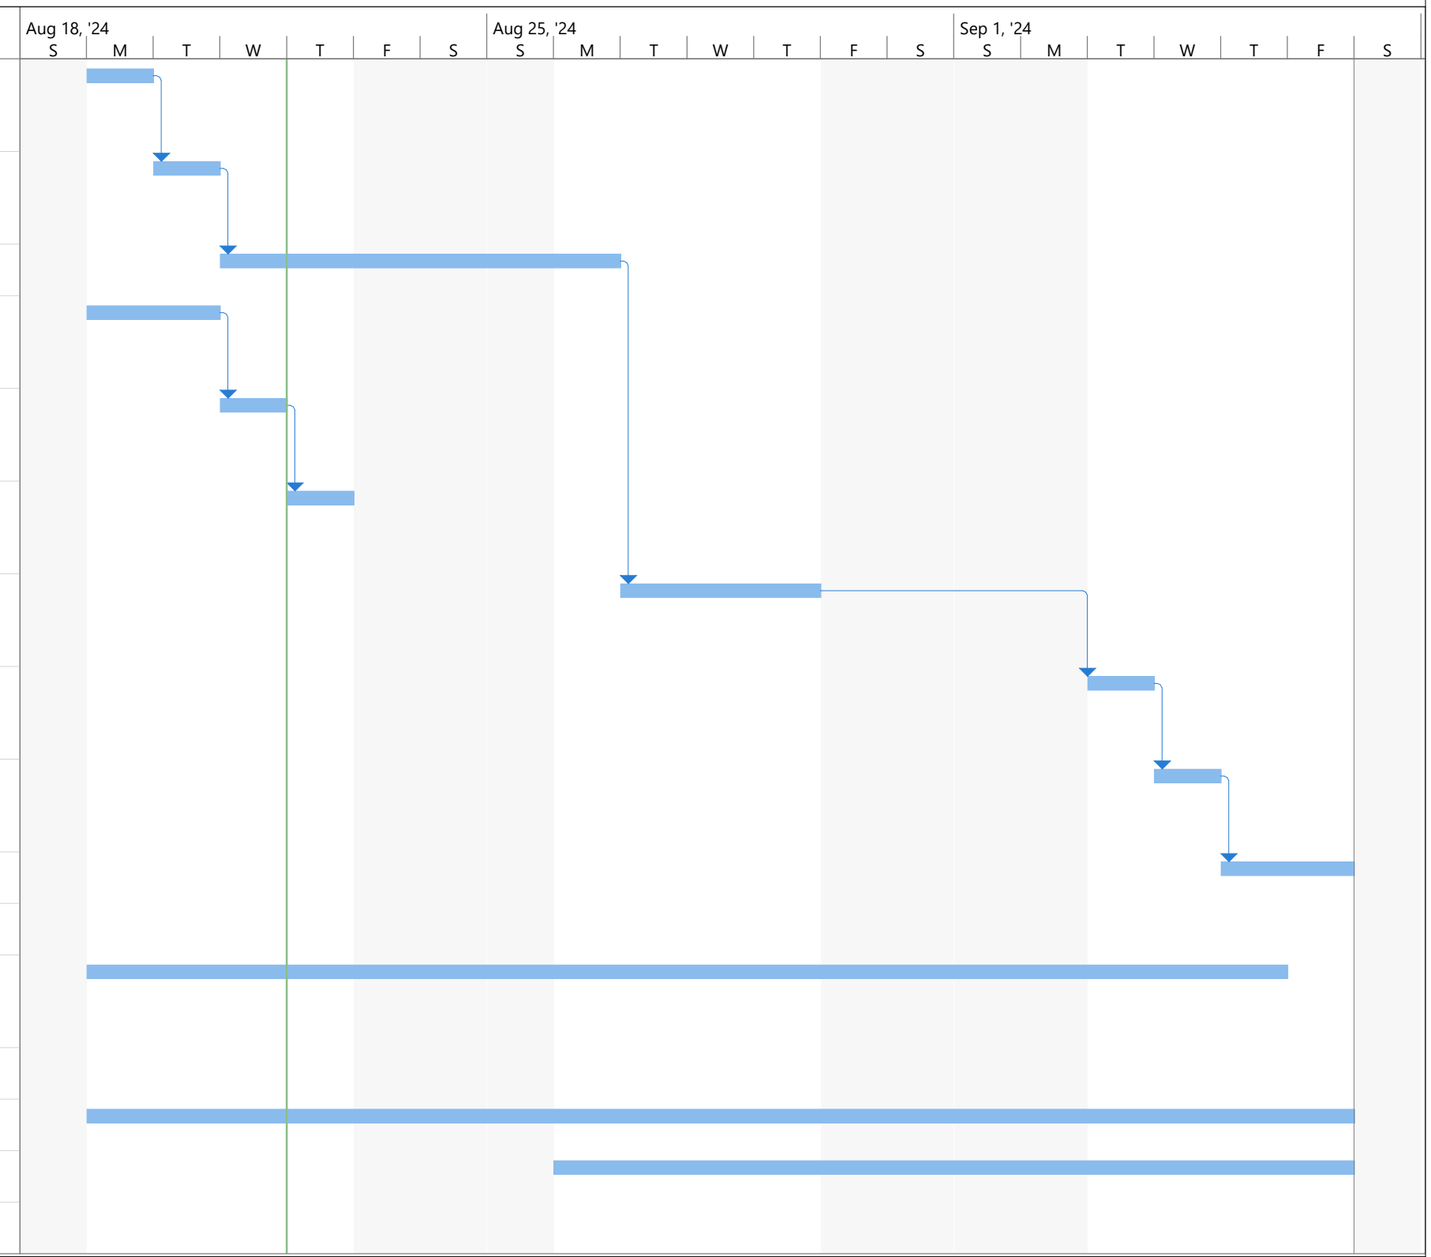
ID	Task Name	Duration	Start	Finish	Predecessors
1	Concrete Repairs - Ramp 2/3 - Rebar & Prep (W.I. 3.1, 3.3, 3.6)	1 day	Mon 8/19/24	Mon 8/19/24	
2	Concrete Repairs - Ramp 2/3 - Pour & Clean (W.I. 3.1, 3.3, 3.6)	1 day	Tue 8/20/24	Tue 8/20/24	1
3	Concrete Curing Period - Ramp 2/3	3 days	Wed 8/21/24	Mon 8/26/24	2
4	Concrete Repairs - Underside Level 2 - Demo (W.I. 4.1, 4.2)	2 days	Mon 8/19/24	Tue 8/20/24	
5	Concrete Repairs - Underside Level 2 - Rebar & Prep (W.I. 4.1, 4.2)	1 day	Wed 8/21/24	Wed 8/21/24	4
6	Concrete Repairs - Underside Level 2 - Pour & Clean (W.I. 4.1, 4.2)	1 day	Thu 8/22/24	Thu 8/22/24	5
7	Concrete Repairs - Ramp 1/2 - Demo (W.I. 3.1, 3.3, 3.6)	3 days	Tue 8/27/24	Thu 8/29/24	3
8	Concrete Repairs - Ramp 1/2 - Rebar & Prep (W.I. 3.1, 3.3, 3.6)	1 day	Tue 9/3/24	Tue 9/3/24	7
9	Concrete Repairs - Ramp 1/2 - Pour & Clean (W.I. 3.1, 3.3, 3.6)	1 day	Wed 9/4/24	Wed 9/4/24	8
10	Concrete Curing Period - Ramp 1/2	2 days	Thu 9/5/24	Fri 9/6/24	9
11					
12	Concrete Repairs - Level 4 (W.I. 3.1, 3.4, 3.7)	11 days	Mon 8/19/24	Thu 9/5/24	
13					
14	Sealant Work - Garage Addition	12 days	Mon 8/19/24	Fri 9/6/24	
15	Expansion Joint - Level 3/4 Addition	8 days	Mon 8/26/24	Fri 9/6/24	
16
